


Site Progress Mobile for Asta Powerproject

Easy progress updating from your mobile devices

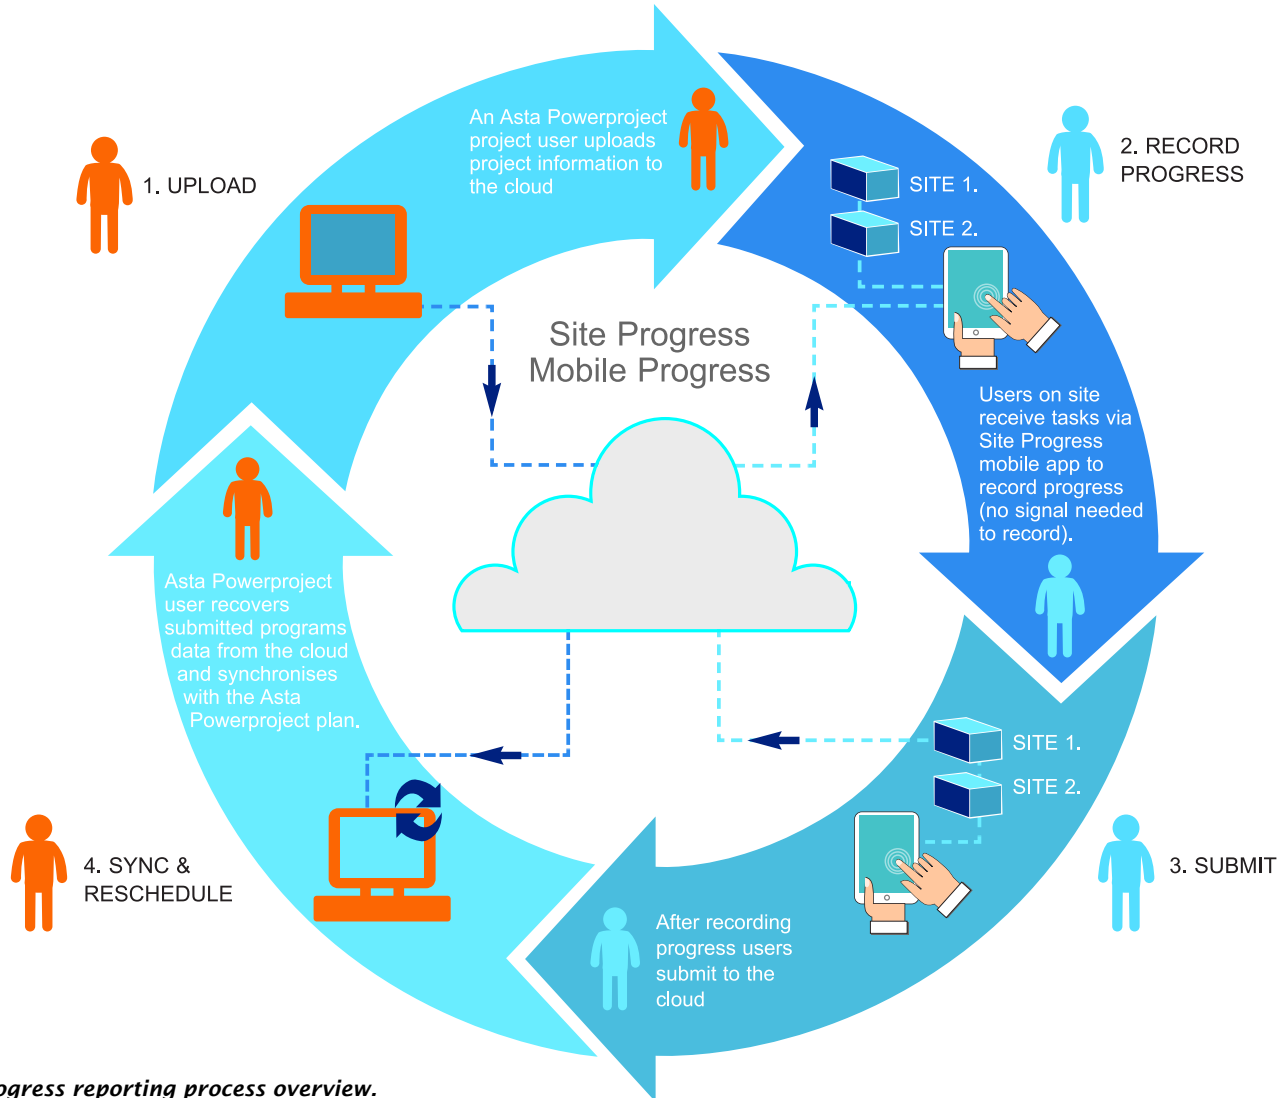

Progress reporting process overview.

Extract and upload

An Asta Powerproject user uploads project information from Asta Powerproject to the Cloud.

They can send selections of data or tasks based on resource allocation. The information is uploaded at the start of the week (or period). Only information relating to those tasks that are due, overdue, or in the near future is uploaded to the Cloud.

Download and record progress

Users are presented with a list of the tasks, or build stages, that relate to them when they open the app. They can record progress (actual dates, percentage complete and remaining duration) which takes place during the week (or period). Notes and photographs can be added to supplement the progress information. Progress can be entered whilst on site even without a phone or Wi-Fi signal.

Submit and upload

Once a user has finished recording progress – typically at the end of the week (or period) – they submit their changes. Project data classified as ‘submitted’ will be uploaded to the Cloud when a phone or Wi-Fi signal is available.

Site Progress Mobile for Asta Powerproject

Download and Integrate

Once 'submitted' project information has been uploaded to the Cloud it is available for the Asta Powerproject user to download.

Reschedule

Once the update has been added as progress in the plan, the project is typically rescheduled.

The process can then be started again, beginning with the extract and upload.

Site Progress Web


In addition to the mobile application, Site Progress can also be accessed via the web.



Turnaround Tasks

Selected chart: \Site Establishment -

Name	Progress (%)	Dates	Days Remaining	Note Photos
Demolish Existing Structures	50	Actual Start: 20/03/2015 Actual Finish: 20/03/2015 Planned Start: 20/03/2015 Planned Finish: 05/04/2015	5	
Excavate to RL	15	Actual Start: 26/03/2015 Actual Finish: 30/03/2015 Planned Start: 30/03/2015 Planned Finish: 20/04/2015	11	
Temporary roads	0	Actual Start: 31/04/2015 Actual Finish: 27/04/2015	5	
Trial Pits, Trial Pit #1	0	Actual Start: 27/04/2015	2	

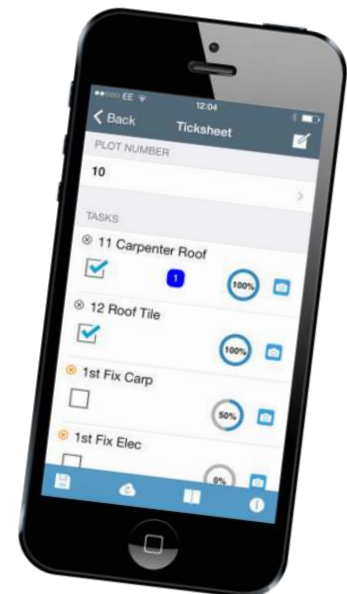

Administration

We provide hosting for the data in the Cloud. When a company signs-up for Site Progress Mobile, an account is created on the Cloud and a number of simultaneous files activated.

Site Progress Mobile components are free to install, with use of the service charged according to the number of active jobs uploaded to the secure cloud storage area.

The fee covers the software licence and technical support.

The active jobs produced are per user and per project. E.g. 3 managers may update different parts of the same project and one of these managers may also update another project - this would contribute 4 active jobs toward the total.

For a quote based on your needs call 01844 261700.

©2017 Elecosoft UK Ltd.

elecosoft.com

Elecosoft[®]

Asta Powerproject: The power behind successful projects
